ID	Task Name	Duration	Start	Finish
1	**Normandy HOA Schedule**	**49 days**	**Wed 11/9/11**	**Mon 1/16/12**
2	**Pre-Con**	**11 days**	**Wed 11/9/11**	**Wed 11/23/11**
3	Notice To Proceed/Signed Contract	1 day	Wed 11/9/11	Wed 11/9/11
4	Pull Permits	3 days	Thu 11/10/11	Mon 11/14/11
5	Order Materials	10 days	Thu 11/10/11	Wed 11/23/11
6	**Building A (north end)**	**5 days**	**Mon 11/21/11**	**Fri 11/25/11**
7	Demolition	1 day	Mon 11/21/11	Mon 11/21/11
8	Paper and Siding	3 days	Tue 11/22/11	Thu 11/24/11
9	Painting	2 days	Thu 11/24/11	Fri 11/25/11
10	**Building B (north end)**	**5 days**	**Tue 11/22/11**	**Mon 11/28/11**
11	Demolition	1 day	Tue 11/22/11	Tue 11/22/11
12	Paper and Siding	3 days	Wed 11/23/11	Fri 11/25/11
13	Painting	2 days	Fri 11/25/11	Mon 11/28/11
14	**Building A (west end)**	**7 days**	**Mon 11/28/11**	**Tue 12/6/11**
15	Set Scaffolding	1 day	Mon 11/28/11	Mon 11/28/11
16	Demolition	2 days	Tue 11/29/11	Wed 11/30/11
17	Paper and Siding	4 days	Wed 11/30/11	Mon 12/5/11
18	Painting	3 days	Fri 12/2/11	Tue 12/6/11
19	**Building A (south end)**	**6 days**	**Tue 12/6/11**	**Tue 12/13/11**
20	Set Scaffolding	1 day	Tue 12/6/11	Tue 12/6/11
21	Demolition	2 days	Wed 12/7/11	Thu 12/8/11
22	Paper and Siding	3 days	Thu 12/8/11	Mon 12/12/11
23	Painting	2 days	Mon 12/12/11	Tue 12/13/11
24	**Building A (east end)**	**7 days**	**Tue 12/13/11**	**Wed 12/21/11**
25	Set Scaffolding	1 day	Tue 12/13/11	Tue 12/13/11
26	Demolition	2 days	Wed 12/14/11	Thu 12/15/11
27	Paper and Siding	4 days	Thu 12/15/11	Tue 12/20/11
28	Painting	3 days	Mon 12/19/11	Wed 12/21/11
29	**Building B (west end)**	**7 days**	**Wed 12/21/11**	**Thu 12/29/11**
30	Set Scaffolding	1 day	Wed 12/21/11	Wed 12/21/11
31	Demolition	2 days	Thu 12/22/11	Fri 12/23/11
32	Paper and Siding	4 days	Fri 12/23/11	Wed 12/28/11
33	Painting	3 days	Tue 12/27/11	Thu 12/29/11
34	**Building B (south end)**	**6 days**	**Thu 12/29/11**	**Thu 1/5/12**

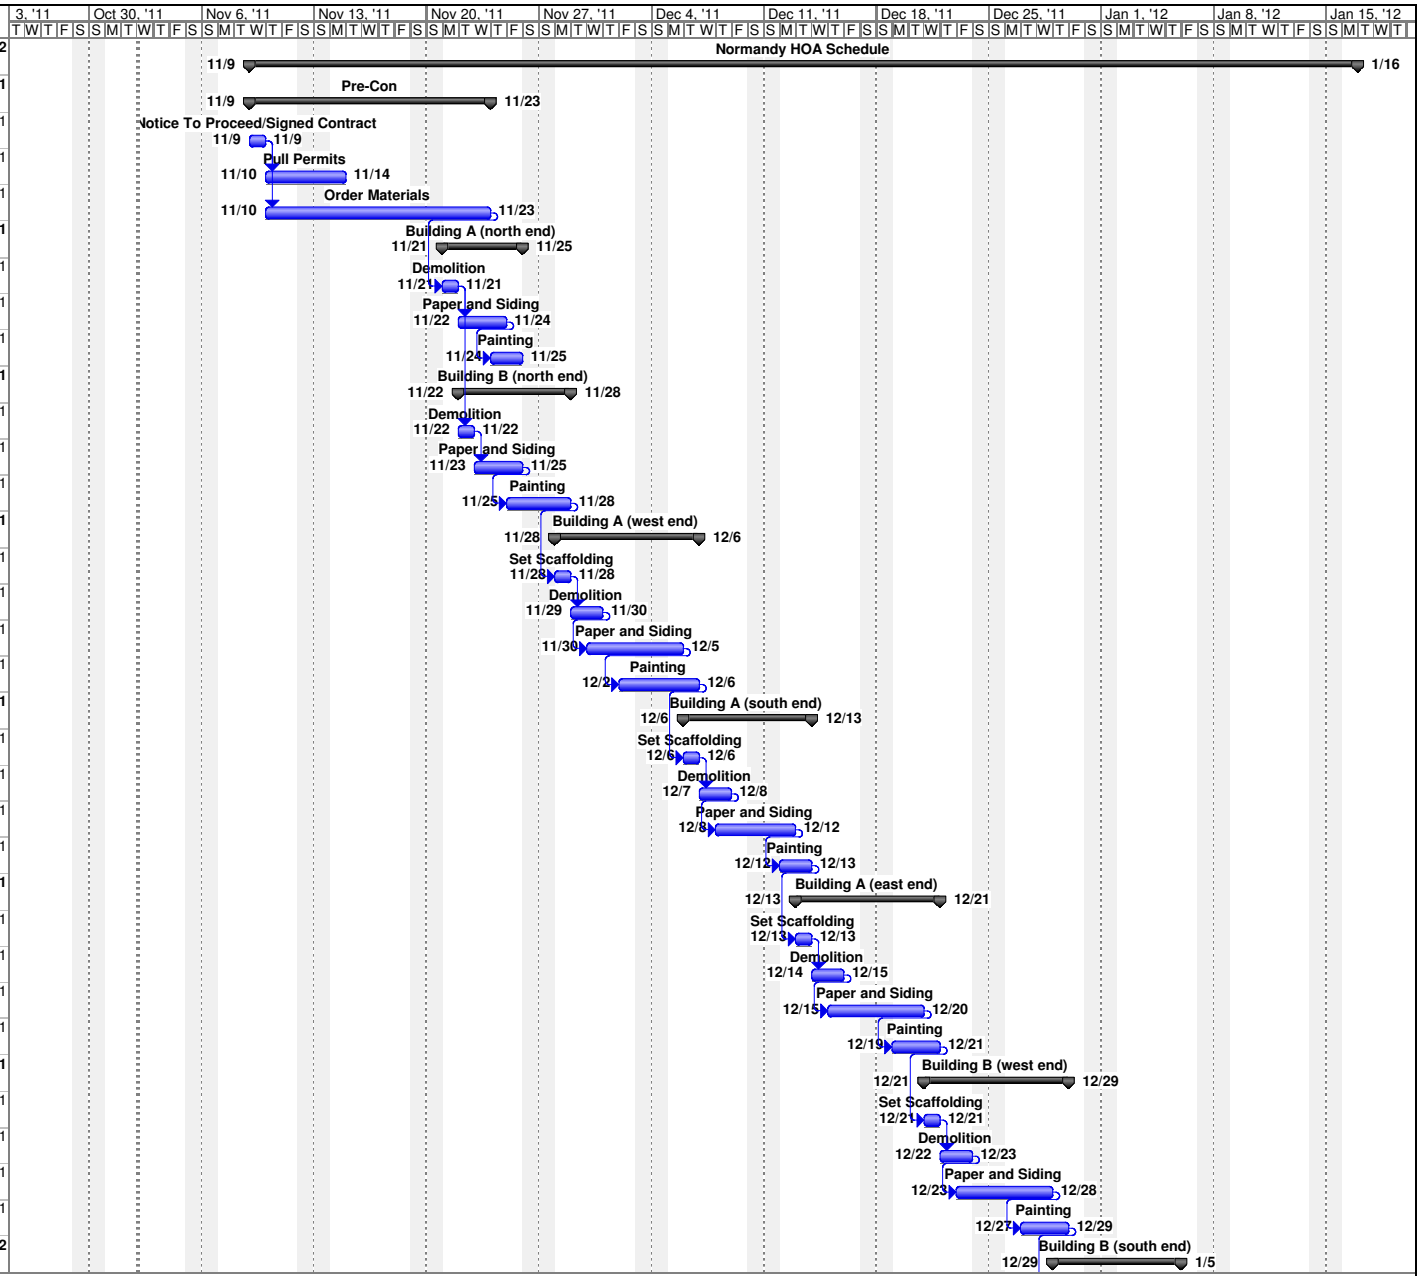

Project: Normandy Sched.1
Date: Wed 11/2/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID	Task Name	Duration	Start	Finish
35	Set Scaffolding	1 day	Thu 12/29/11	Thu 12/29/11
36	Demolition	2 days	Fri 12/30/11	Mon 1/2/12
37	Paper and Siding	3 days	Mon 1/2/12	Wed 1/4/12
38	Painting	2 days	Wed 1/4/12	Thu 1/5/12
39	**Building B (east end)**	**7 days**	**Thu 1/5/12**	**Fri 1/13/12**
40	Set Scaffolding	1 day	Thu 1/5/12	Thu 1/5/12
41	Demolition	2 days	Fri 1/6/12	Mon 1/9/12
42	Paper and Siding	4 days	Mon 1/9/12	Thu 1/12/12
43	Painting	3 days	Wed 1/11/12	Fri 1/13/12
44	**Final Walk & punch List**	**3 days**	**Thu 1/12/12**	**Mon 1/16/12**
45	Perfom pick up list	3 days	Thu 1/12/12	Mon 1/16/12

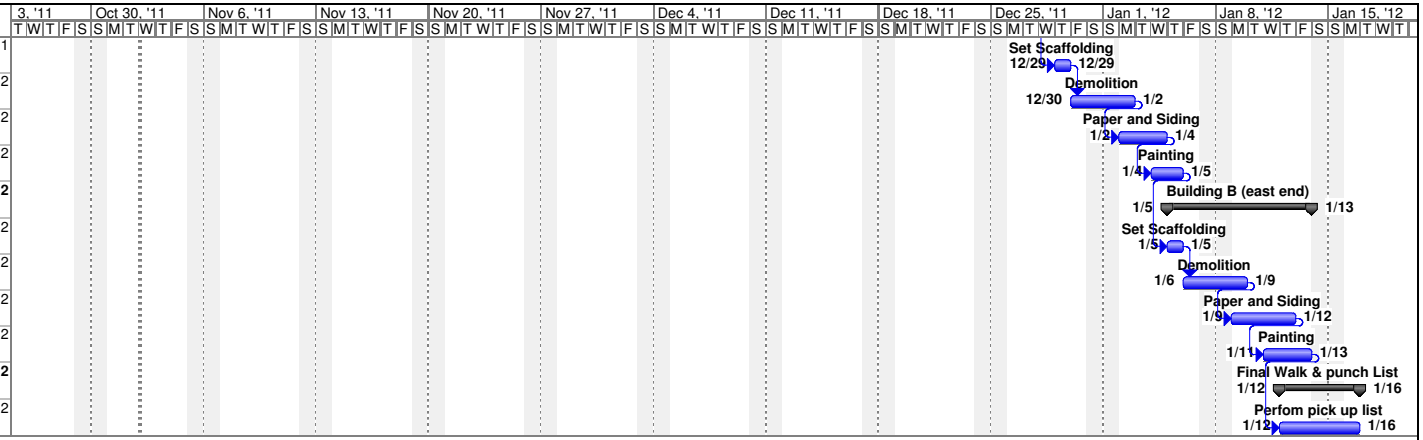

Project: Normandy Sched.1
Date: Wed 11/2/11

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
